Name	Duration	Start	Finish
NTP Received	1 day	Thu 5/28/20	Thu 5/28/20
LOIs Sent	3 days	Fri 5/29/20	Tue 6/2/20
Mobilize	1 day	Fri 5/29/20	Fri 5/29/20
Survey	3 days	Tue 6/2/20	Thu 6/4/20
Clear and Grub	1 day	Fri 6/5/20	Fri 6/5/20
Over-Excavation	10 days	Mon 6/8/20	Fri 6/19/20
Infill	4 days	Mon 6/22/20	Thu 6/25/20
Excavate Foundations	2 days	Wed 6/24/20	Thu 6/25/20
Form Footings	3 days	Fri 6/26/20	Tue 6/30/20
Footing Rebar Placement	2 days	Tue 6/30/20	Wed 7/1/20
Pour & Cure Footings	5 days	Thu 7/2/20	Mon 7/6/20
Form North Wall	5 days	Tue 7/7/20	Mon 7/13/20
Place Rebar in North Wall	3 days	Thu 7/9/20	Mon 7/13/20
Pour Concrete Wall	5 days	Tue 7/14/20	Sat 7/18/20
Form Pilasters	3 days	Mon 7/20/20	Wed 7/22/20
Pilaster Rebar Placement	2 days	Tue 7/21/20	Wed 7/22/20
Pilaster Anchor Bolt Placement	1 day	Wed 7/22/20	Wed 7/22/20
Pour Pilasters	5 days	Thu 7/23/20	Mon 7/27/20
Metal Bollards (Anchored to Footing	3 days	Tue 7/28/20	Thu 7/30/20
Form & Place Rebar - Elec Vault Pad	1 day	Tue 7/28/20	Tue 7/28/20
Pour Elec Vault Pads	5 days	Wed 7/29/20	Sun 8/2/20
Backfill Foundations	2 days	Mon 8/3/20	Tue 8/4/20
Trench and Install UG Elec	5 days	Wed 8/5/20	Tue 8/11/20
Backfill Elec Trenches	1 day	Wed 8/12/20	Wed 8/12/20
Form Elec Vault Walls	2 days	Thu 8/13/20	Fri 8/14/20
Place Rebar - Electrical Vault Walls	1 day	Fri 8/14/20	Fri 8/14/20
Pour Elec Vault Walls	5 days	Sat 8/15/20	Wed 8/19/20
Trench and Install Interior Sanitary	3 days	Thu 8/20/20	Mon 8/24/20
Underground Inspection	2 days	Tue 8/25/20	Wed 8/26/20
Backfill Underground Utilities	1 day	Thu 8/27/20	Thu 8/27/20
Form Trench Drain	3 days	Mon 8/31/20	Wed 9/2/20
Prep SOG Soils	1 day	Fri 8/28/20	Fri 8/28/20
SOG Rebar	3 days	Mon 8/31/20	Wed 9/2/20
Pour and Cure SOG	5 days	Thu 9/3/20	Mon 9/7/20
Erect Steel	6 days	Tue 9/8/20	Tue 9/15/20
Steel Angle Supports for Mech	1 day	Tue 9/15/20	Tue 9/15/20
Set Joists	3 days	Wed 9/16/20	Fri 9/18/20
Set HM Frames	1 day	Tue 9/29/20	Tue 9/29/20
Install Decking	4 days	Fri 9/18/20	Wed 9/23/20
Structural Stud Framing	7 days	Thu 9/24/20	Fri 10/2/20
Set MAU	2 days	Thu 9/24/20	Fri 9/25/20

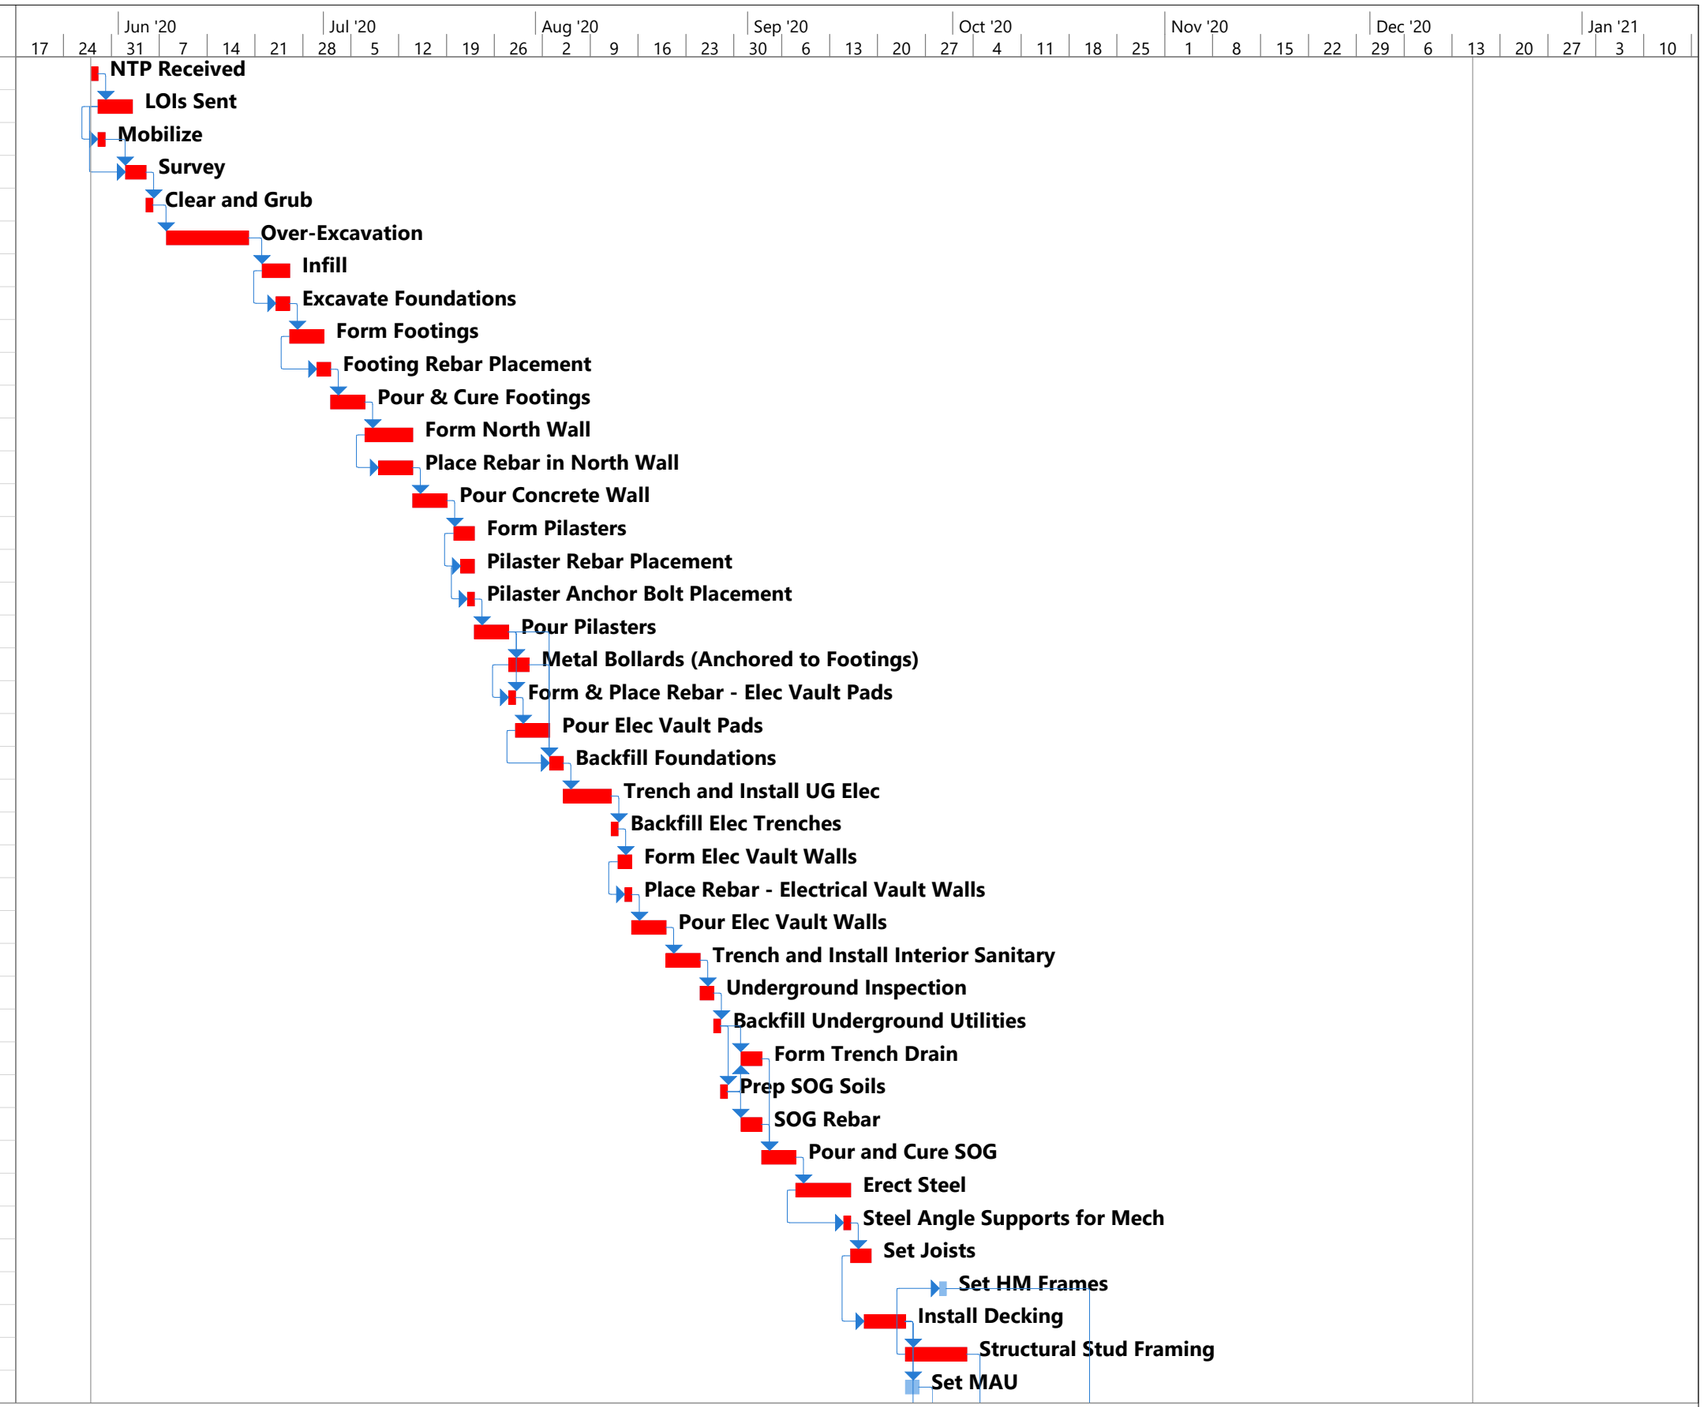

Construction Project Addition
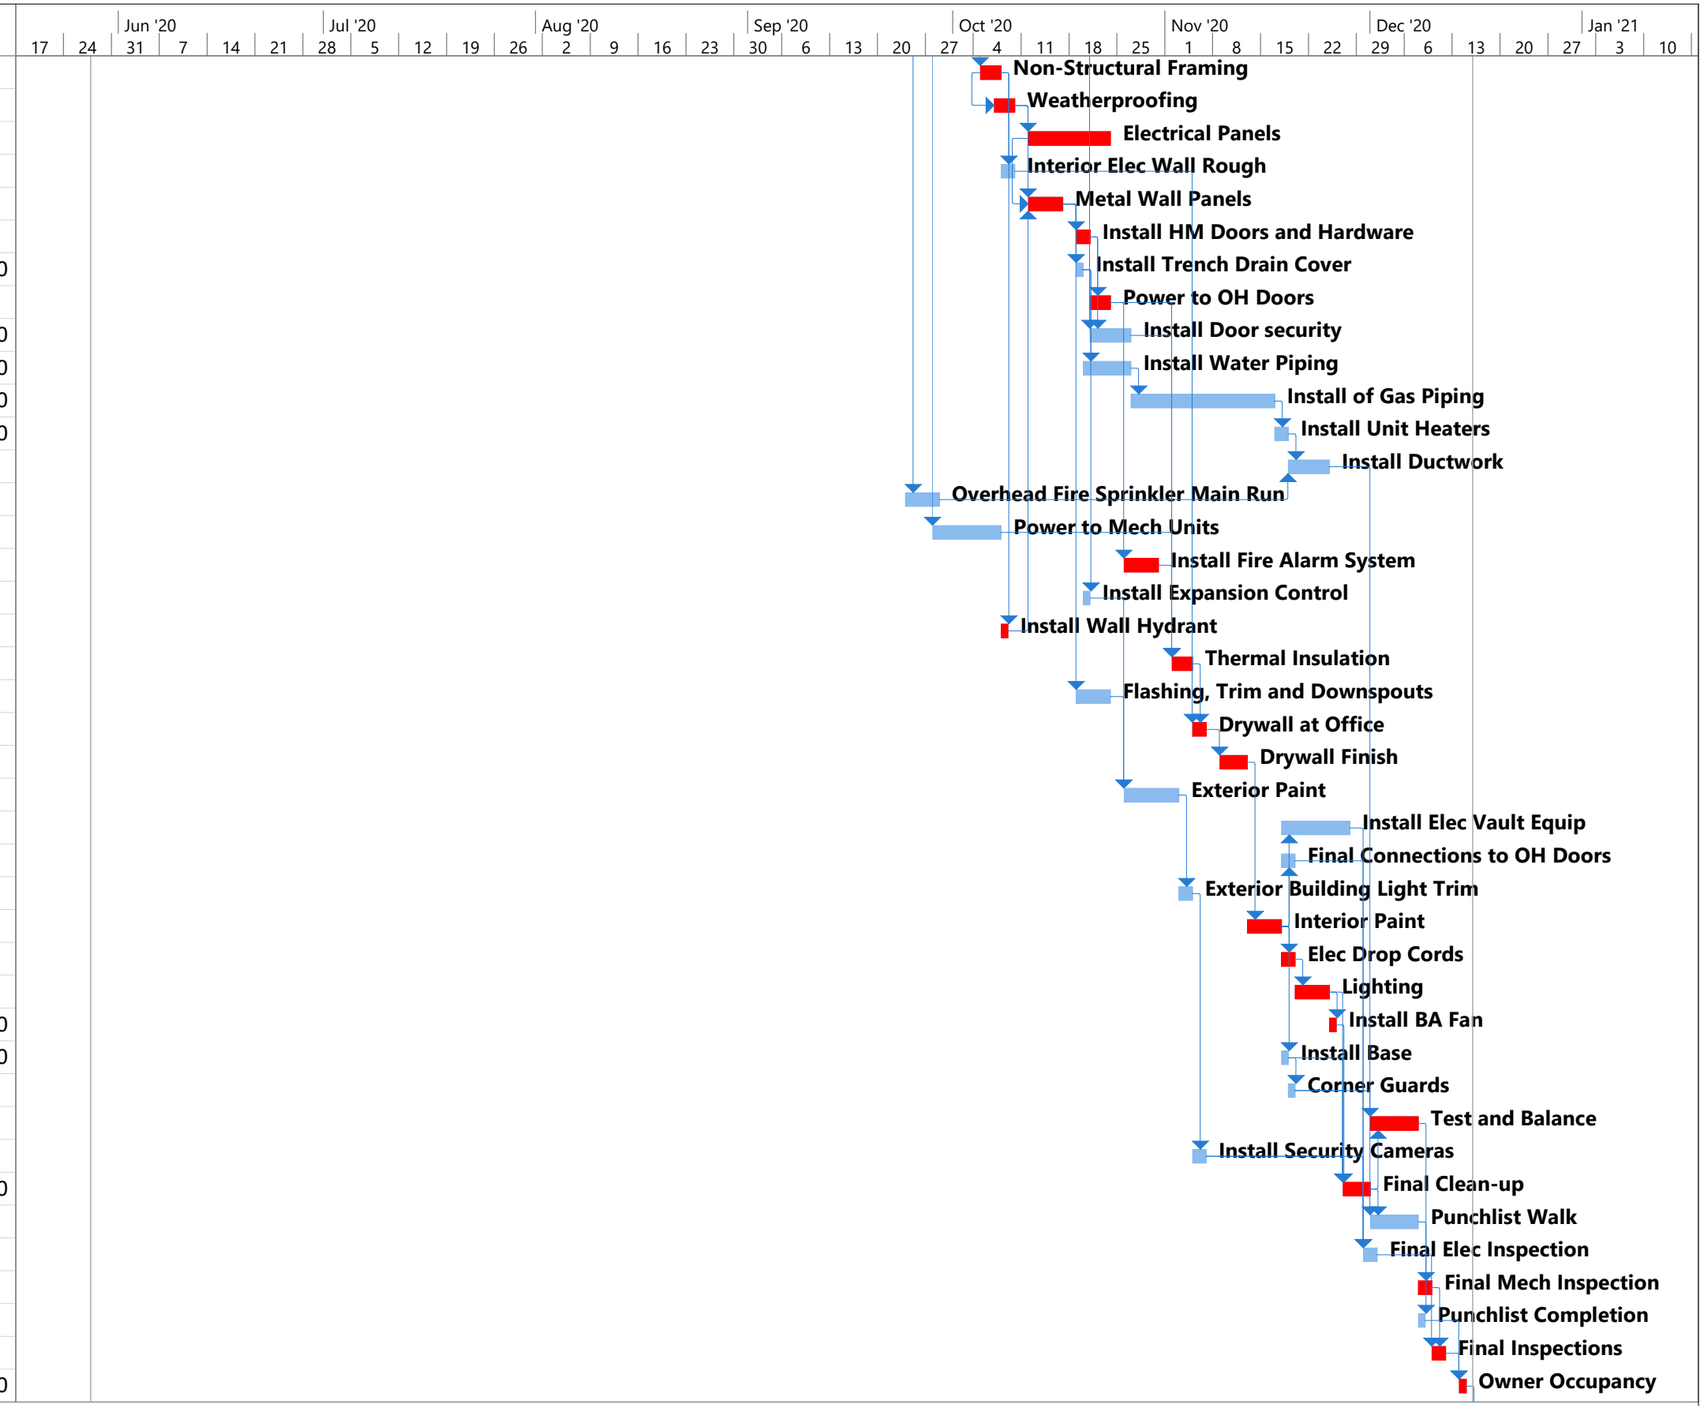
Name	Duration	Start	Finish
Non-Structural Framing	3 days	Mon 10/5/20	Wed 10/7/20
Weatherproofing	3 days	Wed 10/7/20	Fri 10/9/20
Electrical Panels	10 days	Mon 10/12/20	Fri 10/23/20
Interior Elec Wall Rough	2 days	Thu 10/8/20	Fri 10/9/20
Metal Wall Panels	5 days	Mon 10/12/20	Fri 10/16/20
Install HM Doors and Hardware	2 days	Mon 10/19/20	Tue 10/20/20
Install Trench Drain Cover	1 day	Mon 10/19/20	Mon 10/19/20
Power to OH Doors	3 days	Wed 10/21/20	Fri 10/23/20
Install Door security	4 days	Wed 10/21/20	Mon 10/26/20
Install Water Piping	5 days	Tue 10/20/20	Mon 10/26/20
Install of Gas Piping	15 days	Tue 10/27/20	Mon 11/16/20
Install Unit Heaters	2 days	Tue 11/17/20	Wed 11/18/20
Install Ductwork	4 days	Thu 11/19/20	Tue 11/24/20
Overhead Fire Sprinkler Main Run	3 days	Thu 9/24/20	Mon 9/28/20
Power to Mech Units	8 days	Mon 9/28/20	Wed 10/7/20
Install Fire Alarm System	5 days	Mon 10/26/20	Fri 10/30/20
Install Expansion Control	1 day	Tue 10/20/20	Tue 10/20/20
Install Wall Hydrant	1 day	Thu 10/8/20	Thu 10/8/20
Thermal Insulation	3 days	Mon 11/2/20	Wed 11/4/20
Flashing, Trim and Downspouts	5 days	Mon 10/19/20	Fri 10/23/20
Drywall at Office	2 days	Thu 11/5/20	Fri 11/6/20
Drywall Finish	4 days	Mon 11/9/20	Thu 11/12/20
Exterior Paint	6 days	Mon 10/26/20	Mon 11/2/20
Install Elec Vault Equip	7 days	Wed 11/18/20	Fri 11/27/20
Final Connections to OH Doors	2 days	Wed 11/18/20	Thu 11/19/20
Exterior Building Light Trim	2 days	Tue 11/3/20	Wed 11/4/20
Interior Paint	3 days	Fri 11/13/20	Tue 11/17/20
Elec Drop Cords	2 days	Wed 11/18/20	Thu 11/19/20
Lighting	3 days	Fri 11/20/20	Tue 11/24/20
Install BA Fan	1 day	Wed 11/25/20	Wed 11/25/20
Install Base	1 day	Wed 11/18/20	Wed 11/18/20
Corner Guards	1 day	Thu 11/19/20	Thu 11/19/20
Test and Balance	5 days	Tue 12/1/20	Mon 12/7/20
Install Security Cameras	2 days	Thu 11/5/20	Fri 11/6/20
Final Clean-up	2 days	Fri 11/27/20	Mon 11/30/20
Punchlist Walk	5 days	Tue 12/1/20	Mon 12/7/20
Final Elec Inspection	2 days	Mon 11/30/20	Tue 12/1/20
Final Mech Inspection	2 days	Tue 12/8/20	Wed 12/9/20
Punchlist Completion	1 day	Tue 12/8/20	Tue 12/8/20
Final Inspections	2 days	Thu 12/10/20	Fri 12/11/20
Owner Occupancy	1 day	Mon 12/14/20	Mon 12/14/20
