ID	Name	Duration	Start	Finish	Total Float
1	NTP Received	1 day	Thu 5/28/20	Thu 5/28/20	-3 days
2	LOIs Sent	3 days	Fri 5/29/20	Tue 6/2/20	-3 days
3	Mobilize	1 day	Fri 5/29/20	Fri 5/29/20	-2 days
4	Survey	3 days	Tue 6/2/20	Thu 6/4/20	-3 days
5	Clear and Grub	1 day	Fri 6/5/20	Fri 6/5/20	-3 days
6	Over-Excavation	10 days	Mon 6/8/20	Fri 6/19/20	-3 days
7	Infill	4 days	Mon 6/22/20	Thu 6/25/20	-3 days
8	Excavate Foundations	2 days	Wed 6/24/20	Thu 6/25/20	-3 days
9	Form Footings	3 days	Fri 6/26/20	Tue 6/30/20	-3 days
10	Footing Rebar Placement	2 days	Tue 6/30/20	Wed 7/1/20	-3 days
11	Pour & Cure Footings	5 days	Thu 7/2/20	Mon 7/6/20	-5 days
12	Form North Wall	5 days	Tue 7/7/20	Mon 7/13/20	-2 days
13	Place Rebar in North Wall	3 days	Thu 7/9/20	Mon 7/13/20	-2 days
14	Pour Concrete Wall	5 days	Tue 7/14/20	Sat 7/18/20	-4 days
15	Form Pilasters	3 days	Mon 7/20/20	Wed 7/22/20	-3 days
16	Pilaster Rebar Placement	2 days	Tue 7/21/20	Wed 7/22/20	-3 days
17	Pilaster Anchor Bolt Placement	1 day	Wed 7/22/20	Wed 7/22/20	-3 days
18	Pour Pilasters	5 days	Thu 7/23/20	Mon 7/27/20	-5 days
19	Metal Bollards (Anchored to Fo	3 days	Tue 7/28/20	Thu 7/30/20	-3 days
20	Form & Place Rebar - Elec Vault	1 day	Tue 7/28/20	Tue 7/28/20	-3 days
21	Pour Elec Vault Pads	5 days	Wed 7/29/20	Sun 8/2/20	-5 days
22	Backfill Foundations	2 days	Mon 8/3/20	Tue 8/4/20	-3 days
23	Trench and Install UG Elec	5 days	Wed 8/5/20	Tue 8/11/20	-3 days
24	Backfill Elec Trenches	1 day	Wed 8/12/20	Wed 8/12/20	-3 days
25	Form Elec Vault Walls	2 days	Thu 8/13/20	Fri 8/14/20	-3 days
26	Place Rebar - Electrical Vault W	1 day	Fri 8/14/20	Fri 8/14/20	-3 days
27	Pour Elec Vault Walls	5 days	Sat 8/15/20	Wed 8/19/20	-3 days
28	Trench and Install Interior Sanit	3 days	Thu 8/20/20	Mon 8/24/20	-3 days
29	Underground Inspection	2 days	Tue 8/25/20	Wed 8/26/20	-3 days
30	Backfill Underground Utilities	1 day	Thu 8/27/20	Thu 8/27/20	-3 days
31	Form Trench Drain	3 days	Mon 8/31/20	Wed 9/2/20	-3 days
32	Prep SOG Soils	1 day	Fri 8/28/20	Fri 8/28/20	-3 days
33	SOG Rebar	3 days	Mon 8/31/20	Wed 9/2/20	-3 days
34	Pour and Cure SOG	5 days	Thu 9/3/20	Mon 9/7/20	-5 days
35	Erect Steel	6 days	Tue 9/8/20	Tue 9/15/20	-2 days
36	Steel Angle Supports for Mech	1 day	Tue 9/15/20	Tue 9/15/20	-2 days
37	Set Joists	3 days	Wed 9/16/20	Fri 9/18/20	-2 days
38	Set HM Frames	1 day	Tue 9/29/20	Tue 9/29/20	17 days
39	Install Decking	4 days	Fri 9/18/20	Wed 9/23/20	-2 days
40	Structural Stud Framing	7 days	Thu 9/24/20	Fri 10/2/20	-2 days
41	Set MAU	2 days	Thu 9/24/20	Fri 9/25/20	15 days

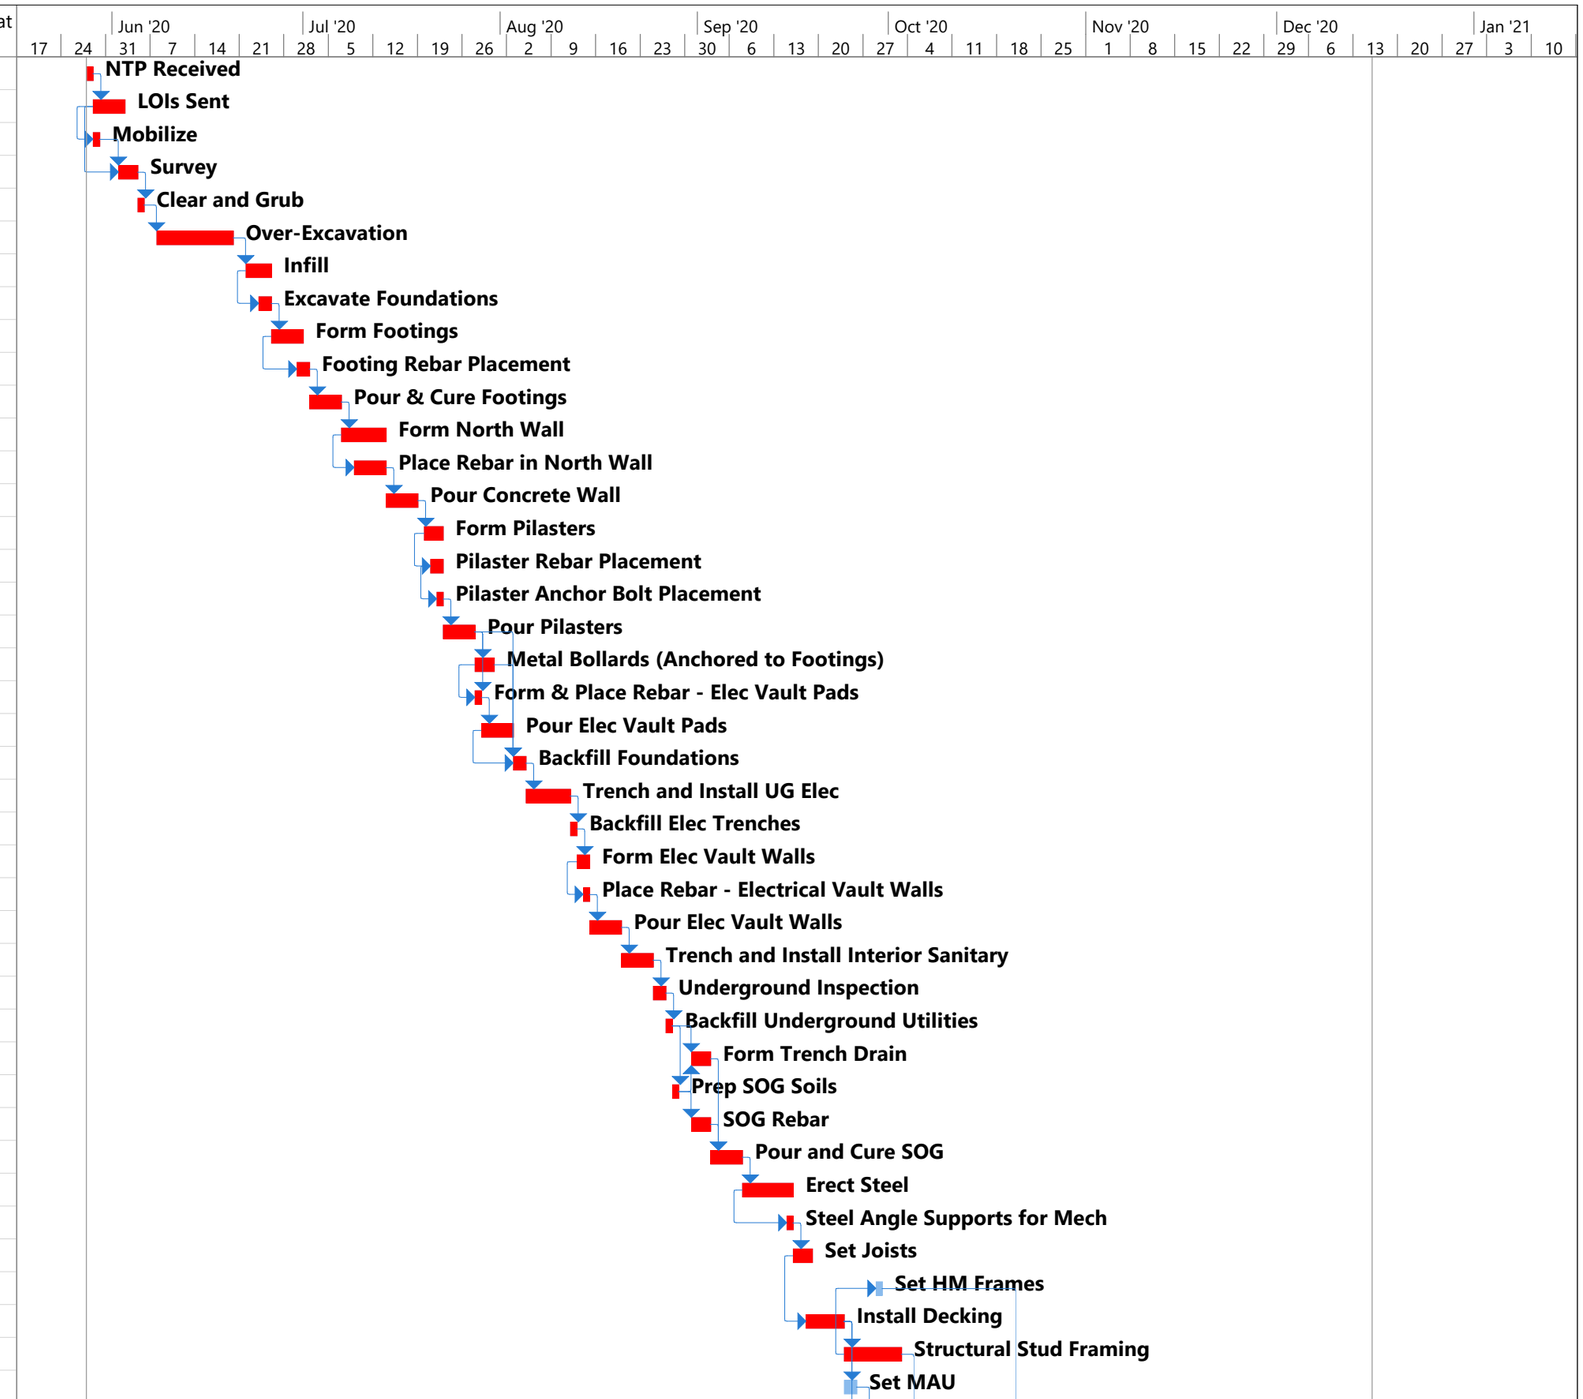

Construction Project Addition
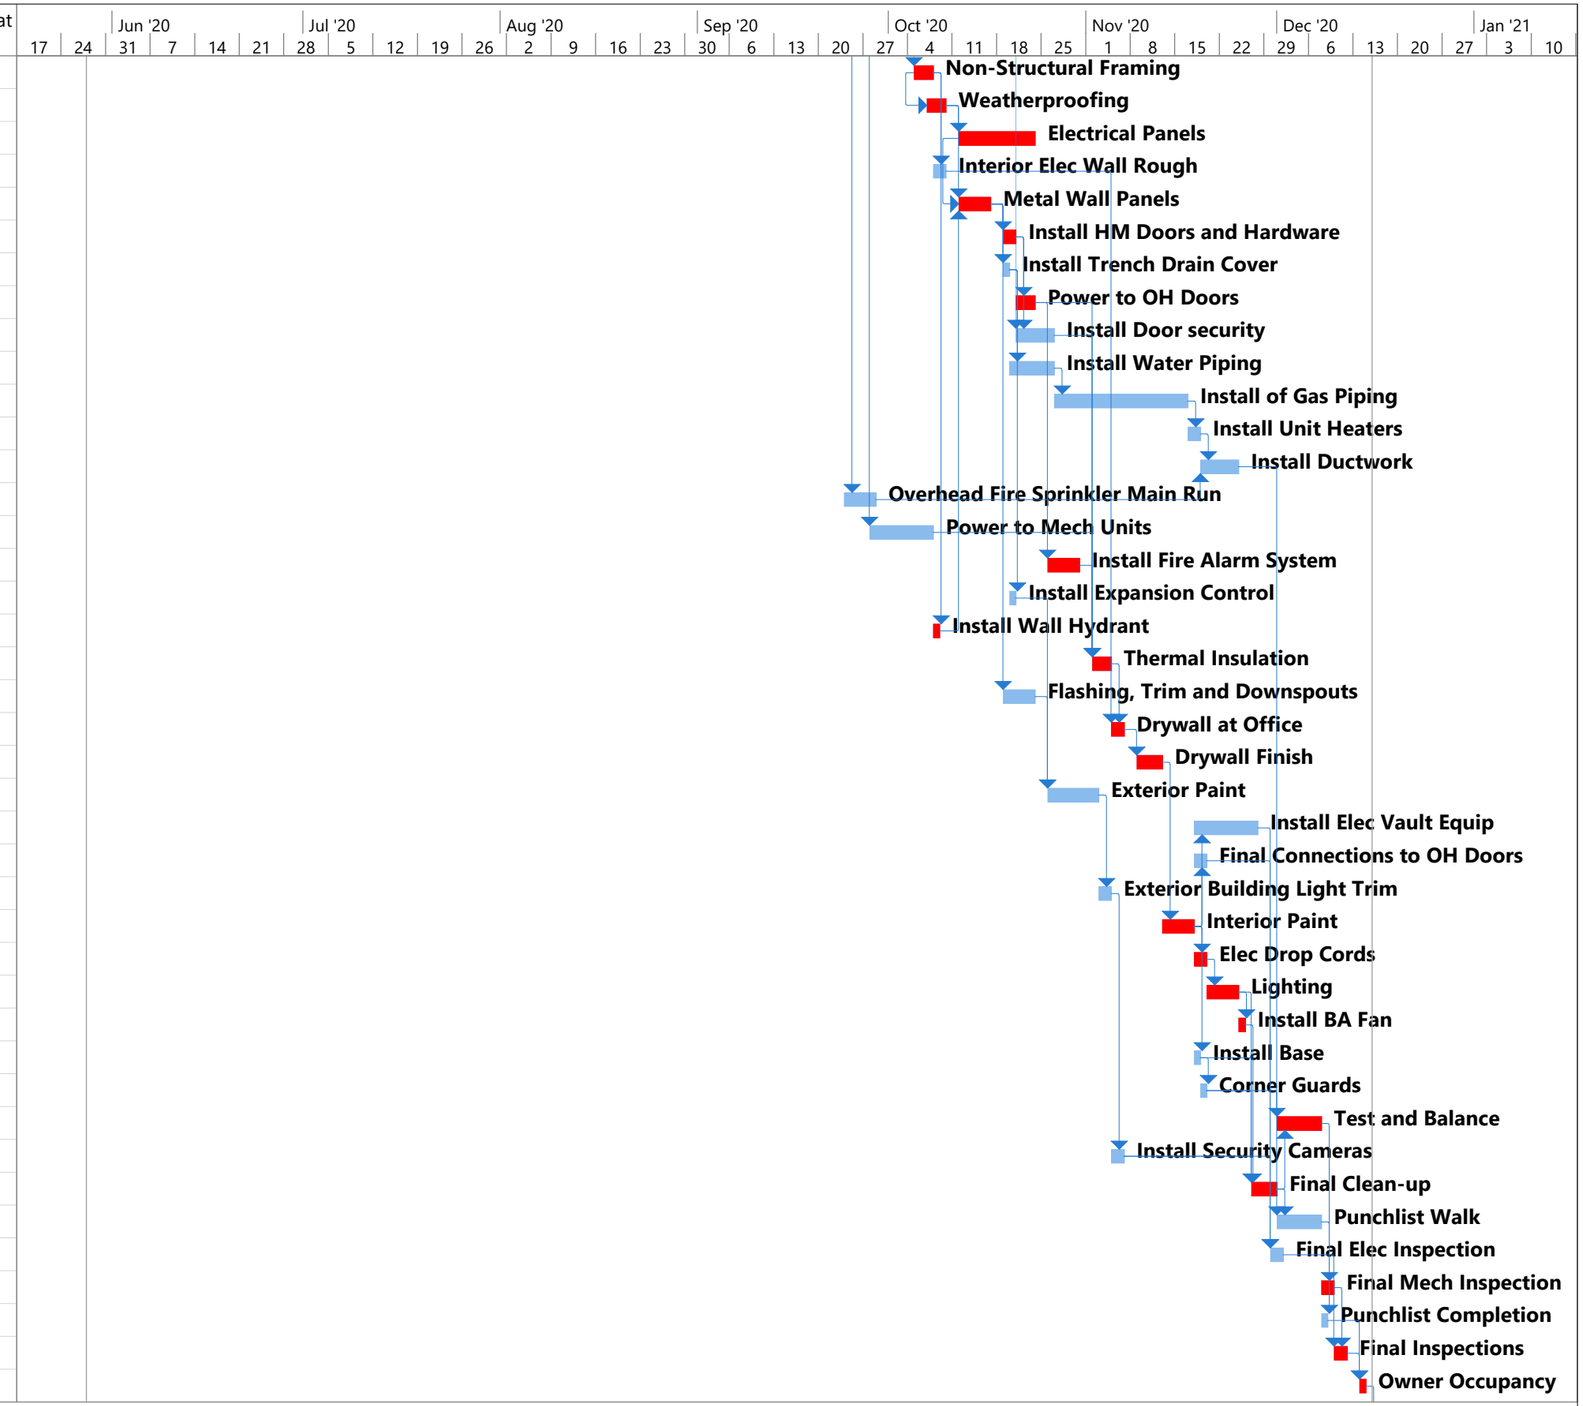
ID	Name	Duration	Start	Finish	Total Float
42	Non-Structural Framing	3 days	Mon 10/5/20	Wed 10/7/20	-2 days
43	Weatherproofing	3 days	Wed 10/7/20	Fri 10/9/20	-2 days
44	Electrical Panels	10 days	Mon 10/12/20	Fri 10/23/20	-2 days
45	Interior Elec Wall Rough	2 days	Thu 10/8/20	Fri 10/9/20	16 days
46	Metal Wall Panels	5 days	Mon 10/12/20	Fri 10/16/20	-2 days
47	Install HM Doors and Hardware	2 days	Mon 10/19/20	Tue 10/20/20	-2 days
48	Install Trench Drain Cover	1 day	Mon 10/19/20	Mon 10/19/20	1 day
49	Power to OH Doors	3 days	Wed 10/21/20	Fri 10/23/20	-2 days
50	Install Door security	4 days	Wed 10/21/20	Mon 10/26/20	2 days
51	Install Water Piping	5 days	Tue 10/20/20	Mon 10/26/20	1 day
52	Install of Gas Piping	15 days	Tue 10/27/20	Mon 11/16/20	1 day
53	Install Unit Heaters	2 days	Tue 11/17/20	Wed 11/18/20	1 day
54	Install Ductwork	4 days	Thu 11/19/20	Tue 11/24/20	1 day
55	Overhead Fire Sprinkler Main R	3 days	Thu 9/24/20	Mon 9/28/20	38 days
56	Power to Mech Units	8 days	Mon 9/28/20	Wed 10/7/20	15 days
57	Install Fire Alarm System	5 days	Mon 10/26/20	Fri 10/30/20	-2 days
58	Install Expansion Control	1 day	Tue 10/20/20	Tue 10/20/20	14 days
59	Install Wall Hydrant	1 day	Thu 10/8/20	Thu 10/8/20	-1 day
60	Thermal Insulation	3 days	Mon 11/2/20	Wed 11/4/20	-2 days
61	Flashing, Trim and Downspouts	5 days	Mon 10/19/20	Fri 10/23/20	11 days
62	Drywall at Office	2 days	Thu 11/5/20	Fri 11/6/20	-2 days
63	Drywall Finish	4 days	Mon 11/9/20	Thu 11/12/20	-2 days
64	Exterior Paint	6 days	Mon 10/26/20	Mon 11/2/20	11 days
65	Install Elec Vault Equip	7 days	Wed 11/18/20	Fri 11/27/20	4 days
66	Final Connections to OH Doors	2 days	Wed 11/18/20	Thu 11/19/20	9 days
67	Exterior Building Light Trim	2 days	Tue 11/3/20	Wed 11/4/20	11 days
68	Interior Paint	3 days	Fri 11/13/20	Tue 11/17/20	-2 days
69	Elec Drop Cords	2 days	Wed 11/18/20	Thu 11/19/20	-2 days
70	Lighting	3 days	Fri 11/20/20	Tue 11/24/20	-2 days
71	Install BA Fan	1 day	Wed 11/25/20	Wed 11/25/20	-2 days
72	Install Base	1 day	Wed 11/18/20	Wed 11/18/20	2 days
73	Corner Guards	1 day	Thu 11/19/20	Thu 11/19/20	2 days
74	Test and Balance	5 days	Tue 12/1/20	Mon 12/7/20	-2 days
75	Install Security Cameras	2 days	Thu 11/5/20	Fri 11/6/20	11 days
76	Final Clean-up	2 days	Fri 11/27/20	Mon 11/30/20	-2 days
77	Punchlist Walk	5 days	Tue 12/1/20	Mon 12/7/20	1 day
78	Final Elec Inspection	2 days	Mon 11/30/20	Tue 12/1/20	4 days
79	Final Mech Inspection	2 days	Tue 12/8/20	Wed 12/9/20	-2 days
80	Punchlist Completion	1 day	Tue 12/8/20	Tue 12/8/20	1 day
81	Final Inspections	2 days	Thu 12/10/20	Fri 12/11/20	-2 days
82	Owner Occupancy	1 day	Mon 12/14/20	Mon 12/14/20	-2 days
